Life Academy Seismic Evaluation and Relocation Timeline Analysis

Division of Facilities Planning and Management



Table of Contents

- 1) Goal
- 2) Seismic Review Analysis & The End Product
 - A) What is the End Product?
 - B) Detailed Tasks Associated with Analysis
 - C) Seismic Review Schedule
- 3) Site Evaluation & Timeline Analysis
 - A) New Portable Campus
 - B) District Owned Sites
 - C) Options for New Portable Campus
 - D) Typical Schedule for New Portable Campus
 - E) New Portable Campus Timeline
 - F) District Owned Facilities
 - G) Other Potential Sites
 - H) Typical Relocation Schedule
 - I) District Owned Facilities Timeline
- 4) Recommendation



Facilities Goal

Field Act Facility for Life Academy ASAP, by August 2008



Seismic Review Analysis

A) What is the end Product?

 The creation of an Evaluation & Criteria report for submittal to DSA

Retrofit Design to correct deficiencies

Cost Estimate



Seismic Review Analysis


B) Detailed Tasks Associated with Analysis

```
Arrange project introduction meeting with DSA
     (1 - 2 weeks)
Geotechnical Investigation: BSE-1 and BSE-2 spectra, prior to building evaluation.
     (6-8 weeks)
Building evaluation: Accessibility, Seismic/Structural, Mechanical, and Electrical reviews resulting
an Evaluation & Design Criteria Report.
     (16-20 weeks)
DSA review of Report.
     (4-6 weeks)
Arrange meeting with DSA to discuss Evaluation & Design Criteria Report
     (1-2 weeks)
Adjust and revise Report if necessary.
     (2-3 weeks)
Schematic Design to show remedies for deficiencies.
     (8 weeks)
7a. Meeting w/DSA with possible revisions to Evaluation & Design Criteria Report
Cost Estimate
     (2-3 weeks)
Oakland Unified School District Review.
     (4 weeks)
```



Seismic Review Analysis

C) Seismic Review Schedule

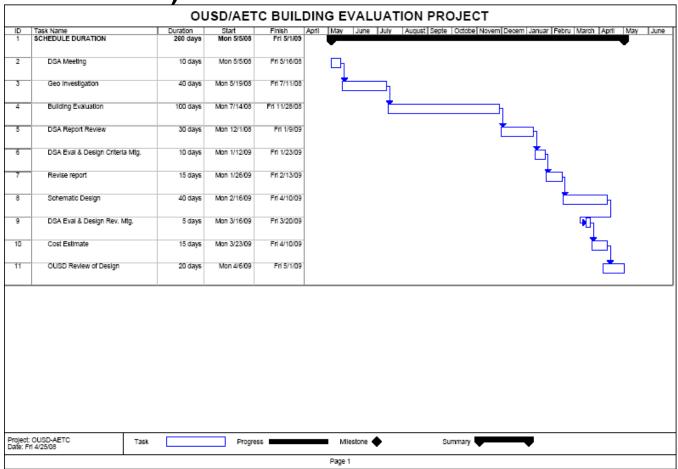



A) New Portable Campus

- 1) Requires Site Acquisition
- 2) Possible environmental cleanup
- 3) Requires Architectural planning & regulatory agency review
- 4) Requires full construction project

B) District Owned Sites

- 1) Requires space planning
- 2) Requires tenant improvements
- 3) Requires Multiple moves




C) Options for New Portable Campus as presented by Life Academy:

- 1) Jack London Aquatic Center
- 2) Lot across From Jack London Square
- 3) City Park next to Garfield Elementary.
- 4) Portables at Life Academy's current site.
- 5) Portables across from Life Academy's current site.
- 6) Portables across from Cesar Chavez.
- 7) East Bay Blue Print site.



D) Typical Schedule for New Portable Campus

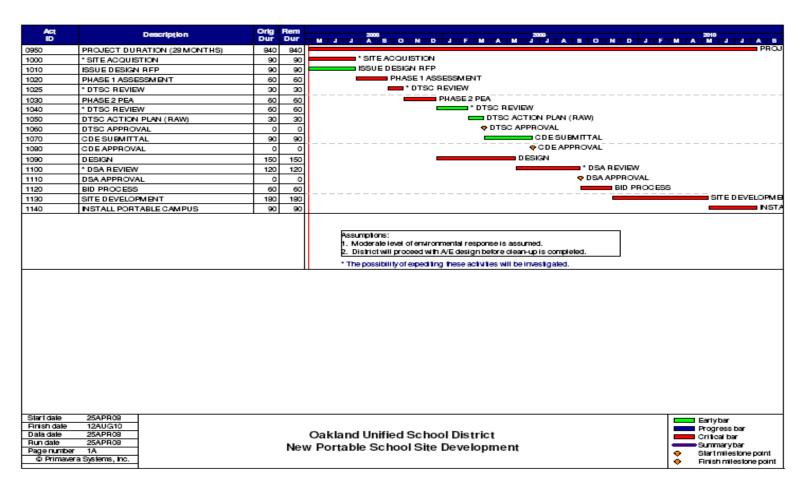



E) New Portable Campus Timeline

Given a decision by today, April 30, 2008, a new portable campus at any of these or other Non District Owned sites would require up to 29 months until occupancy.



F) District Owned Facilities

1) King Estates

- Adequate classrooms
- Not in San Antonio District; Poor Transit Access
- Potential multi-year availability

2) Carter

- Needs two portables (Fire Access)
- Not San Antonio District; Good Transit Access
- Limited to 1 year availability

3) Harper

- Needs limited interior reconfigurations
- Near San Antonio District: Good Transit Access
- Up to 3 year availability
- Does not impact Downtown Education Center Project



F) District Owned Facilities-cont

4) Calvin Simmons

- Space Available if Peralta Creek does not take in 6th or 7th grade and 3 additional portables installed
- Near San Antonio District
- Minimal Impact to existing program Potential multi year availability

5) 900 High Street

- Non-Option
- No classroom spaces at this site
- Would require demolition of warehouse



G) Other Potential Sites

- 1) Laney
 - Availability Unknown
 - Would require up to 14 classrooms for 2-3 years
 - Unknown Cost Impacts??



District Owned Property Typical Relocation Schedule

ın	In the	I 5 I	0	F: - 1	February	March	April	May	June	July	August	September	October	November
ID 1	Task Name	Duration 80 days	Start Thu 5/1/08	Finish W ed 8/20/08	1 eu uai y	Iviai ui	Арш	iviay	Jule	July	August	September	Octoba	November
'	SCHEDULEDURATION	ou u ays	111u 3/1/06	W eu a/20/06				Y			_			
2	SPACEPLANNING	25 days	Thu 5/1/08	Wed 6/4/08			0%		Some Ard	: nitect Involver	nent			
3	TENENTIMPROVEMENTS	25 days	Tue 5/27/08	Mon 6/30/08				0%		Install Clock	Bell,Data,Ad	i min Etc		
4	INTERALMOVE OF (E) PRGM.	25 days	Fri 6/20/08	Thu 7/24/08			Coordinate	with Administrati	on 🕌	0	%			
5	MOVE LIFEACADEMY INTO SITE	25 days	Thu 7/17/08	Wed 8/20/08			Move	n bystart of 200	: 8/2009 sessior		0%			



I) District Owned Facilities Timeline

Given a decision by today, April 30, 2008, a District Owned facility could be occupied by Life Academy by start of the 2008/2009 school year.



Recommendation

We strongly recommend vacating the existing Life Academy Bldg and relocating Life Academy to a Field Act Compliant District owned facility.

Abandon pursuit of new portable campus options.

We strongly recommend that the district make a decision this evening.

