



Board Office Use: Legislative File Info.	
File ID Number	22-1351
Introduction Date	6-09-2022
Enactment Number	22-`1202
Enactment Date	6-22-2022 er

Memo

To Measures B, J, and Y Independent Citizens' School Facilities Bond Oversight Committee

From Kyla Johnson-Trammell, Superintendent
Tadashi Nakadegawa, Deputy Chief, Facilities Planning and Management

Board Meeting Date June 9, 2022

Subject Laurel Child Development Center Budget Increase \$2.5 million - June 9, 2022 - Division of Facilities Planning and Management

Action Presentation for Approval Laurel Child Development Center Budget Increase of \$2.5 million

Background Overview of four Bids were received, this indicates a competitive, market value bid, lowest Bid is from a contractor who has successfully completed multiple projects with Oakland Unified School District.

Bid Tabulation:

- | | |
|---------------------------------|--------------|
| 1. Arntz Builders | \$14,288,436 |
| 2. Thompson/Focon JV | \$16,077,751 |
| 3. JUV, Inc | \$16,795,000 |
| 4. CWS Construction Group, Inc. | \$16,995,000 |

The low bid does exceed our Measure Y project budget. The attached presentation shows the market factors contributing to this extraordinary price increase from the last estimate completed at the time that the project was submitted to DSA. Given this extraordinary increase in construction costs we are not recommending rebidding as costs are still trending up significantly.

Recommendation Approval of the Laurel Child Development Center Budget Increase of \$2.5 million, June 9, 2022. This budget increase allows the award of the low bid and start of construction this summer.

Fiscal Impact \$2.5 million to be allocated the Laurel CDC project out of the Measure Y Bond Program Contingency Fund

Attachment Resolution No. 2122-0234
Exhibit A – Laurel Child Development Center Budget Increase - June 9, 2022

**RESOLUTION
OF THE
BOARD OF EDUCATION**

OF THE OAKLAND UNIFIED SCHOOL DISTRICT

Resolution No. 2122-0234

Laurel Child Development Center Budget Increase June 9, 2022

WHEREAS, overview: four Bids were received, this indicates a competitive, market value bid;

WHEREAS, an extraordinary spike in construction costs over the past year has resulted in bids that exceed the Measure Y allocation for this project;

WHEREAS, the Inflation Rates for construction have increased costs over 25% 2019 rates;

WHEREAS, Staff have analyzed the options for rebidding and scope reduction and recommend proceeding with the project by increasing the budget by \$2.5 million out of the Measure Y Bond Program Contingency;

NOW, THEREFORE, BE IT RESOLVED; the Board hereby adopts the Approval Laurel Child Development Center Budget Increase of \$2.5 million, June 9, 2022.

PASSED AND ADOPTED by the Board of Education of the Oakland Unified School District this 22nd day of June, 2022; by the following vote, to wit:

PREFERENTIAL AYE: None

PREFERENTIAL NAY: None

PREFERENTIAL ABSTAINED: None

AYES: Aimee Eng, VanCedric Williams, Mike Hutchinson, Clifford Thompson, Vice President Benjamin "Sam" Davis, President Gary Yee

NAYS: None

ABSTAINED: None

RECUSED: None

ABSENT: (Vacancy), Samantha Pal (Student Director), Natalie Gallegos Chavez (Student Director)

CERTIFICATION

We hereby certify that the foregoing is a full, true and correct copy of a Resolution passed at a Regular Meeting of the Board of Education of the Oakland Unified School District held on June 22, 2022.

Board Office Use: Legislative File Info.	
File ID Number	22-1351
Introduction Date	6-9-2022
Enactment Number	22-1202
Enactment Date	6/22/2022 er

OAKLAND UNIFIED SCHOOL DISTRICT

G.S.D. Yee

Gary Yee, President, Board of Education

K. Johnson-Trammell

Kyla Johnson-Trammell
Superintendent and Secretary, Board of Education

Exhibit "A" - Exhibit A – Laurel Child Development Center Budget Increase - June 9, 2022



OAKLAND UNIFIED
SCHOOL DISTRICT
Community Schools, Thriving Students



FACILITIES DEPARTMENT

Laurel Child Development Center Budget Increase Citizen's Bond Oversight Committee – June 9, 2022



www.ousd.org



@OUSDnews

Overview

1. *Four Bids were received, this indicates a competitive, market value bid.*
2. *Lowest Bid is from a known contractor who has done business with the district.*
3. *Lowest Bid was approx. \$1.75M below next lowest bid.*
4. *Likely cause of low bid is efficiencies of working on multiple projects with in the district.*


Bid Tabulation

1.	<i>Arntz Builders</i>	<i>\$14,288,436</i>
2.	<i>Thompson/Focon JV</i>	<i>\$16,077,751</i>
3.	<i>JUV, Inc</i>	<i>\$16,795,000</i>
4.	<i>CWS Construction Group, Inc.</i>	<i>\$16,995,000</i>

Original Measure Y Budget

1. Construction (Hard/Soft)	\$ 12,661,500	72%
2. Contingency/Allowances	\$ 2,338,500	28%
Total	\$15,000,000	

Current Inflation Rates

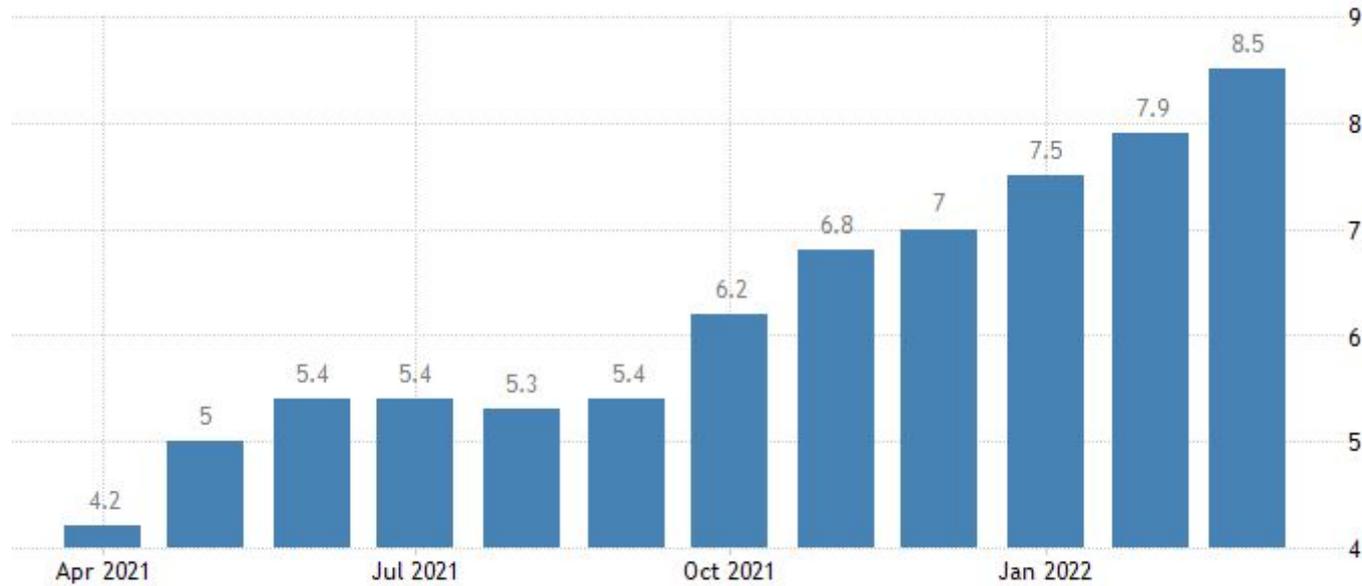

TRADINGECONOMICS.COM | U.S. BUREAU OF LABOR STATISTICS

Transportation Costs

Year-over-year change in domestic U.S. freight expenditures



Construction Escalation

Recent data from the U.S. Census Bureau shows construction costs went up by **17.5%** year-over-year from 2020 to 2021, the largest spike in this data from year to year since 1970. 2021's costs were also more than 23% higher than pre-pandemic 2019. Feb. 16, 2020

California Construction Cost Index 2021-2025

Month	2025	2024	2023	2022	2021
January				8151	7090
February				8293	7102
March				8736	7130
April				8903	7150
May					7712
June					7746
July					7892
August					8122
September					7900
October					8080
November					8141
December					8072
Annual % *					13.4%

10% in first
three months

*Annual Percentage is calculated from December to December.

Bid Tabulation- Recent Bids

PROJECT	BID DATE	ENGINEER'S ESTIMATE	LOWEST BID
Claremont MultiPurpose Building	4/13/2022	\$ 13,300,000	\$ 14,685,725
Laurel Child Development Center	4/14/2022	\$ 11,500,000	\$ 13,814,463
Castlemont Fields and Track	5/17/2022	\$ 7,500,000	\$ 8,155,000
MLA: Trust for Public Land Site Improvements	5/26/2022	\$ 1,490,000	\$ 4,100,000

Next Steps

Facilities Committee has forwarded this item with support for approval by the Board of Education to Increase budget by \$2.5m from Measure Y Bond Program Contingency to allow award to the low responsible bidder. The Facilities Committee also requested this item to be presented to the Measures B, J, and Y Independent Citizens' School Facilities Bond Oversight Committee for information.



Quality Schools in Every Neighborhood!



**OAKLAND UNIFIED
SCHOOL DISTRICT**

Community Schools, Thriving Students

1000 Broadway, Suite 300, Oakland, CA 94607

www.ousd.org



@OUSDnews
