



# 2026 MEASURE Y REVISION

## SPENDING PLAN AMENDMENT #4 - 2nd Read

Board of Education, June 24, 2026 Meeting  
OUSD Facilities Planning & Management



**OAKLAND UNIFIED  
SCHOOL DISTRICT**  
*Community Schools, Thriving Students*



## Agenda

- Ask of the Committee
- Section One: Context & Achievements
- Section Two: Spending Plan Revisions
- Section Three: Major Facilities Project Updates
- Next Steps



## Ask of the Board

Approve the Measure Y Spending Plan Revision #4, as approved by Facilities Committee





# OUSD Vision and Mission



## VISION

All OUSD students will find joy in their academic experience while graduating with the skills to ensure they are caring, competent, fully-informed, critical thinkers who are prepared for college, career, and community success.



## MISSION

Oakland Unified School District (OUSD) will build a Full Service Community District focused on high academic achievement while serving the whole child, eliminating inequity, and providing each child with excellent teachers, every day.



# Section One

Context and  
Achievements



# Spending Plan Overview

---

**The Capital Spending Plan is a dynamic implementation tool that guides how bond funds are prioritized, sequenced, and managed in alignment with the District’s adopted Facilities Master Plan.** It translates the District’s long-term facilities priorities into a financial roadmap that supports major projects, deferred maintenance needs, and other critical investments across school sites.

The Capital Spending Plan:

- Aligns Measure Y bond resources to the priorities identified in the adopted Facilities Master Plan.
- Provides a **financial roadmap** for sequencing and delivering major capital projects and districtwide investments.
- **Remains dynamic and adaptable**, allowing the District to respond to market conditions, construction escalation, changes in project scope, and evolving District priorities.
- Supports fiscal accountability and transparency through regular review, adoption, adjustment, and monitoring of project budgets and milestones by Facilities Committee, CBOC, and the Board of Education.
- Maintains the financial integrity and long-term health of the Measure Y bond program while balancing community commitments, available resources, and fiduciary responsibilities.



# Capital Program Progress to Date (March 2026)

**225**

Funded Projects

**142**

Completed Projects\*

Measure Y \$239,141,619  
Measure J \$462,924,147  
Measure B \$450,190,734

Total spent through 3/31/26  
across bond measures:  
**\$1,152,256,500\***



\*Approximate





# Expanding Our Funding Portfolio to Support Healthy, Safe, and Joyful Schools



## PROGRAMS

- Appliance Management Incentive Program
- Developer Fees
- Expanded Learning Opportunities Program
- Energy Incentive
- Office of Public School Construction
- PG&E Government and K-12 Program

## GRANTS

- CalSHAPE
- CalFire
- Kitchen Infrastructure Training



# Facilities Master Plan - T-Shaped Investment Strategy



Tiers of Implementation and Types of Projects under T-Shaped Investment Strategy



# Facilities Master Plan - Tiered Districtwide Investments

## Tier 1 – High Investment Area Prioritize Health, Safety, and Core Learning Environment

**Purpose:** Invest in infrastructure to keep schools functional, safe, and compliant.

**Examples:**

- HVAC modernization, heat mitigation, and air quality improvements
- Water quality, plumbing, electrical infrastructure
- Restroom modernization
- Fencing, lighting, seismic, and safety upgrades
- Deferred Maintenance (roofs, floors, etc.)

## Tier 2 – Medium Investment Build Whole-Child Experience, Educational Equity, Long Term Innovation

**Purpose:** Modernize learning environments to better serve students and support academic success.

**Examples:**

- TK/Early Childhood expansions
- Specialized Program STEM, arts, CTE, etc.
- Special education space upgrades
- Multipurpose rooms, dining hall, and kitchen modernization
- Technology infrastructure for 21st-century classrooms

## Tier 3 – Sustain Investments Maintain Partnership and Long-Term Sustainability

**Purpose:** Maintain inspiring, community-connected, and sustainable campuses.

**Examples:**

- Athletic fields and gym modernizations
- Living schoolyards and shaded outdoor learning spaces
- Energy efficiency, solar, and EV infrastructure

● Yellow highlights identify areas of increased investments based on district needs and priorities.




# Section Two

## Spending Plan Revisions



# Budget Check Points for Major Projects

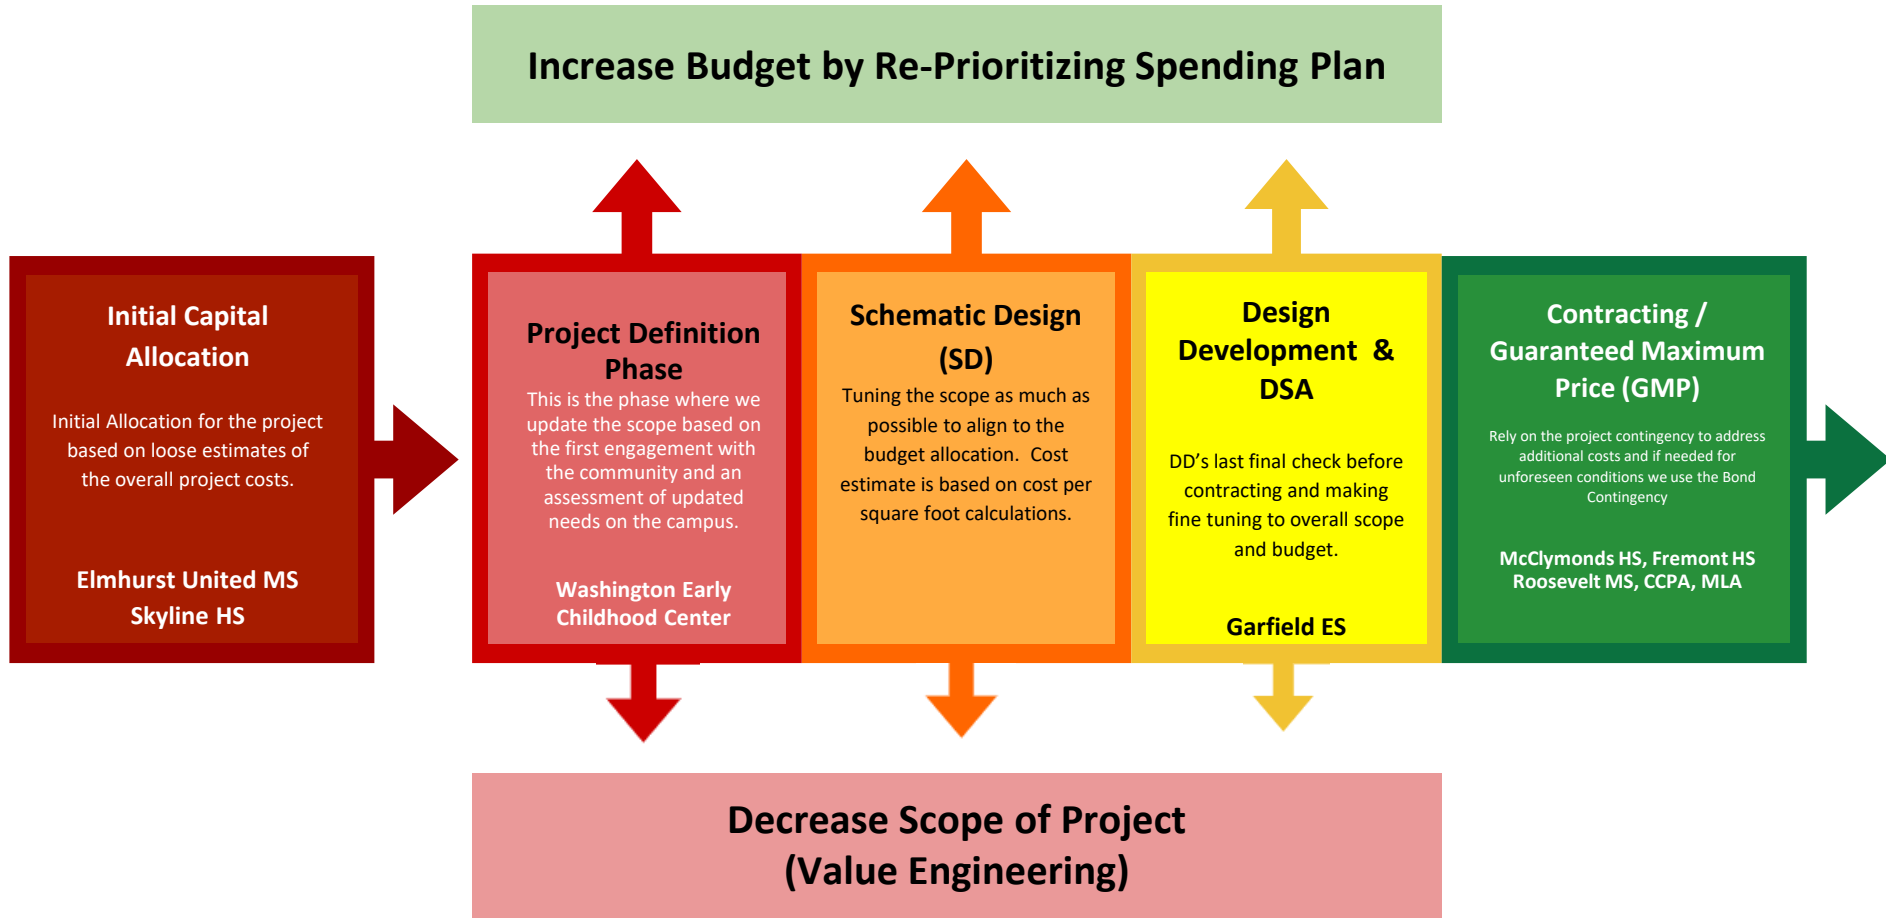



# Contingency & Earned Interest Allocation



## Contingency and Earned Interest Allocation are Aligned to Existing Strategic Goals

### 1. Honor Commitments to Oakland Voters and School Communities

Preserve the core scope and educational intent of projects previously committed to Oakland voters and named school communities in Measure B, J and Y Bond Language that was approved by the Board.

### 2. Prioritize Investments Using the Adopted 2026 Facilities Master Plan

Align capital investments with the Oakland Unified School District Facilities Master Plan to ensure resources are directed to the updated District's highest-priority facility needs.

### 1. Invest in Projects that Both Align to Master Plan and also Offset General Fund Costs

Prioritize capital projects, such as solar and other operational efficiency initiatives, that reduce ongoing utility and operating expenses and create long-term cost avoidance for the General Fund.

### 2. Maintain Deferred Maintenance Support (No Changes)

Maintain funding for deferred maintenance to ensure the District has resources to replace systems that reach end of life and are being prioritized in the Comprehensive Maintenance Plan until the Board restores a sustainable annual deferred maintenance program.



## Measure Y Bond Contingency Overview

Facilities Master Plan / Bond Contingency

1



Initial Bond Contingency

**\$73.5M**

10% of the Measure Y Bond

Full Benchmark Amount



2



Current Contingency

**\$62.8M**



**\$10.7M**

Decrease from Initial Amount



3



Remaining Contingency and Allocation Summary

**\$30.3M**

Remaining from Original Contingency

**\$30.3M**  
Remaining Contingency

**\$32.5M**  
Allocated  
Major Projects &  
District-Wide Investments

Fourth Update

**\$10.7M**

Previous Allocations

Original Bond Contingency (\$73.5M)



The remaining balance of **\$30.3M** from the original contingency is preserved for unforeseen circumstances and future priorities.



# Bond Measure Y Contingency-Key Takeaway

## ***Is the overall contingency large enough to support the program after the 3rd draw?***

With the bond program roughly three-quarters complete, the remaining \$30.3 M contingency represents approximately 16.5% of the estimated remaining program value. Major projects also retain embedded project-level contingencies, consistent with CASBO<sup>^</sup>-informed best practices.

**This is a strong remaining contingency position** based on industry standards\* that recognize that the bond contingency needs decline as project scope, estimates, bids, and construction progress become more defined. Maintaining \$30.3M at this stage provides meaningful protection for unforeseen conditions, escalation, emergency needs, and future Board priorities.

## **Future Known Priorities for the Remaining \$30.3 M**

1st Priority	2nd Priority
<ol style="list-style-type: none"> <li>1. Garfield Project at GMP</li> <li>2. Mandatory Lighting Upgrades</li> <li>3. Heat Mitigation and HVAC Phase 2</li> <li>4. Deferred Maintenance-Electrical</li> <li>5. TK Expansion and TK Hubs</li> </ol>	<ol style="list-style-type: none"> <li>1. Comprehensive Maintenance Plan Projects</li> <li>2. Special Education Program Supports</li> <li>3. Accessibility and Access Investments</li> <li>4. Safety and Electric Door Locking Systems</li> </ol>

*\*This analysis is informed by AIA guidance on construction contingency management, GFOA best practices for capital project monitoring and reporting, and AACE International cost engineering guidance defining contingency as a reserve for uncertain conditions or events.*

*<sup>^</sup>California Association of School Business Officials. CASBO recommends a 12% and 18% total program contingency and our remaining contingency falls within that range.*



# Major Facilities Projects Updates



# Proposed Major Projects Budget Changes



Site Specific Named Projects	Status	Approved Measure Y Budget (March 2025)	Proposed Change Measure Y (May 2026)	Proposed Measure Y Budget (May 2026)	Approved Funding Other Capital Funds (March 2025)	Proposed Funding Increased in other Capital Funds (May 2026)	Total Revised Allocation (May 2026)
<b>Major Projects</b>							
<b>Complete Major Projects</b>							
Claremont MS	Closeout	\$18,000,000	-\$500,000	\$17,500,000	\$3,271,672	\$0	\$20,771,672
Laurel CDC	Complete	\$15,000,000	-\$1,562,657	\$13,437,343	\$3,500,000	\$0	\$16,937,343
1000 Broadway Interim Housing	Complete	\$4,323,532	\$0	\$4,323,532	\$0	\$0	\$4,323,532
Dr. Marcus A. Foster Leadership Center	Closeout	\$55,000,000	\$0	\$55,000,000	\$7,000,000	\$0	\$62,000,000
<b>Active Major Projects</b>							
McClymonds HS	GMP	\$95,750,000	\$12,250,000	\$108,000,000	\$0	\$0	\$108,000,000
Roosevelt MS	Construction	\$90,550,000	\$6,050,000	\$96,600,000	\$1,000,000	\$0	\$97,600,000
Garfield ES (Resolution NO. 2526-0102) Approved	100% DD	\$70,700,000	\$0	\$70,700,000	\$0	\$34,550,000	\$105,250,000
Coliseum College Prep. Academy	GMP	\$55,000,000	\$6,000,000	\$61,000,000	\$13,000,000	\$0	\$74,000,000
Melrose Leadership Academy	GMP	\$36,500,000	\$2,700,000	\$39,200,000	\$3,000,000	\$0	\$42,200,000
Fremont High School	Construction	\$0	\$0	\$0	\$15,000,000	\$7,800,000	\$22,800,000
Washington CDC	New Project - Planning	\$0	\$0	\$0	\$2,000,000	\$18,020,000	\$20,020,000
<b>Future Projects (Draw 4)</b>							
Elmhurst United MS	Planning	\$8,504,796	\$0	\$8,504,796	\$1,495,204	\$0	\$10,000,000
Skyline HS	Planning	\$8,504,796	\$0	\$8,504,796	\$1,495,204	\$0	\$10,000,000
<b>Site Specific Named Projects</b>		<b>\$457,833,124</b>	<b>\$24,937,343</b>	<b>\$482,770,467</b>	<b>\$50,762,080</b>	<b>\$60,370,000</b>	<b>\$593,902,547</b>



Proposed budget changes





# McClymonds HS: Modernization, Stadium Project & Turf Field Replacement



**Approved Budget:** \$95.75 Million

**Proposed Budget Increase:** \$12.25 Million

**Total Proposed Budget:** \$108 Million

**Project Status:** DSA approved in April 2026; Board approved Guaranteed Maximum Price Pending

**Project Scope:**

- Modernized classrooms, breakout spaces, and science labs supporting next-generation teaching and learning
- New gymnasium building with locker rooms, training and weight rooms, equipment storage, and modern athletic support spaces
- Upgraded campus infrastructure including HVAC, plumbing, electrical systems, ADA accessibility, and enhanced safety and security features
- Revitalized campus environment with modern restrooms, collaborative learning spaces, and inclusive outdoor areas for recreation, events, and student gathering

**Funding Sources:** Measure Y

**Rationale for Budget Increase:** See next slide

**Recommendation:** • Allocate \$12.25 Million from Measure Y Contingency





# McClymonds HS: Modernization, Stadium Project & Turf Field Replacement



OAKLAND UNIFIED  
SCHOOL DISTRICT  
Community Schools, Thriving Students

## Rationale for Requested Budget Increase:

The requested increase to the McClymonds Modernization and Turf Field/Track/Stadium Upgrade Project budget from \$95.75 million to \$108 million reflects a combination of construction market escalation, extended regulatory review timelines, unforeseen existing conditions, and refinements to project scope that emerged as design and implementation progressed. The Division of the State Architect (DSA) review process took approximately 15 months rather than the anticipated 7 months, resulting in escalation of costs due to increases in labor and materials.

During DSA review and extensive testing, additional existing conditions and required code corrections were identified, including structural conditions, non-code-compliant walls identified during DSA review, and environmental remediation oversight requirements associated with the field work. The revised budget also incorporates a series of infrastructure and operational enhancements that will improve long-term campus functionality, safety, and reliability, including retaining walls, upgraded field lighting, data and communications infrastructure, clock/speaker systems, security system relocation, and related stadium improvements. The proposed increase will be funded through a combination of interest earnings accrued that have been added to the Program Contingency during the extended DSA review period and bond contingency funds.

The updated contractor estimates for the turf field and stadium improvements needed to remediate the soils reflect significantly higher construction costs than originally projected for similar sized fields, particularly as material pricing and market conditions evolved over the course of the extended approval timeline. The longer overall schedule and incorporation of the stadium project now including a field into the broader modernization project also increased project phasing and coordination costs.





# McClymonds HS: Modernization, Stadium Project & Turf Field Replacement



OAKLAND UNIFIED SCHOOL DISTRICT  
Community Schools, Thriving Students

Project Renderings



Project Profile Page  
Scan to view project details and reports





# CCPA: Expansion/Portable Replacement



**Approved Budget:** \$68 Million

**Proposed Budget Increase:** \$6 Million

**Total Proposed Budget:** \$74 Million

**Project Status:** DSA Approved Increment #1; Awaiting DSA approval from Increment 2; Board approved GMP

**Project Scope:**

- 14 modernized classrooms with breakout spaces and two state-of-the-art science labs
- New gymnasium with training and weight rooms, locker rooms, and equipment storage supporting athletics and physical education
- Modern, private restroom facilities integrated into the new classroom and gymnasium buildings
- Inclusive outdoor spaces designed for flexible learning, student gathering, recreation, and community event

**Funding Sources:** Measure Y \$55 Million; Fund 25 (Developer Fees): \$13 Million

**Rationale for Budget Increase:**

- +\$5M-Identified IT upgrades, escalation in equipment and permitting costs, and accurate costing of design costs and construction management costs.
- +1M-An anticipated \$1M is planned to ensure all outstanding items based on construction activity are resolved at Greenman Field and allow OUSD formally close out the project

**Recommendation:** Allocate \$6 Million from Measure Y Contingency





# CCPA: Expansion/Portable Replacement



OAKLAND UNIFIED SCHOOL DISTRICT  
Community Schools, Thriving Students

Project Renderings



Project Profile Page  
Scan to view project  
details and reports





# Garfield ES: Rebuild and Early Childhood Education Expansion



<b>Approved Budget</b>	\$70.7 Million
<b>Proposed Budget Increase:</b>	No change/Pending DSA Submission
<b>Total Proposed Budget:</b>	\$104.5 Million
<b>Project Status:</b>	100% Design Development; Board approved <a href="#">Resolution No. 2526-0102</a> : Revised Scope, Budget, and Funding Plan
<b>Project Scope:</b>	<ul style="list-style-type: none"> <li>● New PK–5 campus amenities including 30+ classrooms, library, multipurpose room, Family Resource Center, and elimination of temporary portable housing</li> <li>● Expansion of TK/PK capacity from 3 to 7+ classrooms</li> <li>● Modernized healthy building systems including upgraded ventilation, monitoring, insulation, and resilient Title 24-compliant design</li> <li>● <b>Net Zero Energy-ready</b> campus featuring all-electric high-efficiency systems, LED lighting, and battery storage</li> <li>● Play Structures for TK, PK, and for all students at K-5 grade levels</li> <li>● Staff parking and bicycle parking for students, staff, and families</li> </ul>
<b>Funding Sources:</b>	Measure Y: \$70.7 Million; OCI: \$19 Million; Fund 25 (Developer Fees): \$5 Million; Fund 35: \$9.8 Million
<b>Rationale for Budget Increase:</b>	My need additional budget to meet NetZero energy usage after heat pump calculations are completed, increase in security fencing and land entitlement.
<b>Recommendation:</b>	NA





# Garfield ES: Rebuild and Early Childhood Education Expansion



OAKLAND UNIFIED SCHOOL DISTRICT  
Community Schools, Thriving Students



*Project Renderings*

Project Profile Page  
 Scan to view project details and reports






# MLA Maxwell: Expansion/Portable Replacement



<b>Approved Budget:</b>	\$39.5 Million
<b>Proposed Budget Increase:</b>	\$2.7 Million
<b>Total Proposed Budget</b>	\$42.2 Million
<b>Project Status:</b>	Awaiting DSA approval; Board approved Guaranteed Maximum Price
<b>Project Scope:</b>	<ul style="list-style-type: none"> <li>• New middle school building featuring six classrooms, specialized learning spaces, a science lab, and gender-neutral restrooms</li> <li>• Sustainability upgrades including solar panels, battery storage, and new high-efficiency heat pump systems</li> <li>• Campuswide infrastructure improvements including plumbing renovations, fire and life safety enhancements, and seismic retrofitting</li> <li>• Modernized learning environments with upgraded administrative spaces, improved air quality, HVAC systems, and climate-controlled classrooms</li> </ul>
<b>Funding Sources:</b>	Measure Y; Fund 25 (Developer Fees): \$3M
<b>Rationale for Budget Increase:</b>	Expanded project scope to include heat mitigation improvements to building to reduce energy costs and meet Title 24 requirements.

**Recommendation:** Allocate \$2.7 Million from Measure Y Contingency



# MLA Maxwell: Expansion/Portable Replacement



## Project Renderings



Project Profile Page  
Scan to view project  
details and reports





# Roosevelt MS: Modernization



**Approved Budget:** \$91.5 Million

**Proposed Budget Increase:** \$6.1 Million

**Total Proposed Budget:** \$ 97.6 Million

**Project Status:** Building A Alteration - Phase 1, under construction

**Project Scope:**

- New 3,400 sq. ft. science building providing modern labs and hands-on STEM learning opportunities
- Renovated classrooms, interiors, and shared spaces creating brighter, modernized learning environments
- Upgraded campus systems including HVAC, lighting, fire alarms, sprinklers, and security improvements supporting safety and comfort
- Structural and outdoor improvements including strengthened buildings, gardens, landscaping, and enhanced student gathering and learning spaces

**Funding Sources:** Measure B, Measure Y

**Rationale for Budget Increase:**

- A \$6.1M for projected design costs in early phase of planning that was lower than industry standard, construction management, Architect/Engineering fees and increase in Inspector fees, DSA fees, move services, furniture, and custodial.

**Recommendation:** Allocate \$6.1 Million from Measure Y Contingency





# Roosevelt MS: Modernization



OAKLAND UNIFIED SCHOOL DISTRICT  
Community Schools, Thriving Students



Project Profile Page  
Scan to view project details and reports





# Fremont HS: Portable, Roof, HVAC Replacement



OAKLAND UNIFIED SCHOOL DISTRICT  
Community Schools, Thriving Students

**Approved Budget**

\$15 Million

**Proposed Budget Increase:**

\$7.8 Million

**Total Proposed Budget:**

\$22.8 Million

**Project Status:**

Construction

**Project Scope:**

- Four new permanent modular classrooms and two modern office spaces supporting teaching, learning, and student services
- Elevator modernization to improve campus accessibility and safety for students, staff, and visitors
- Renovated Foothill Boulevard (“Mac Dre”) parking lot with expanded parking, upgraded lighting, and EV charging infrastructure supporting safety and sustainability

**Funding Sources:**

Measure J: \$18.3 Million; Fund 35: \$4.5M

**Rationale for Budget Increase:**

- Expanded project scope including roofing replacement and heat mitigation improvements.
- Roof is highest ranked issue on Comprehensive Maintenance Plan.
- Additional electrification and mechanical system installations required for full functionality.

**Recommendation:**

- Allocate \$3.3 Million from Measure J (Fremont New Construction Phase 1-4)
- Allocate \$4.5 Million from Fund 35 (State Reimbursement-Fremont Project)






# Fremont HS: Portable, Roof, HVAC Replacement



OAKLAND UNIFIED SCHOOL DISTRICT  
Community Schools, Thriving Students

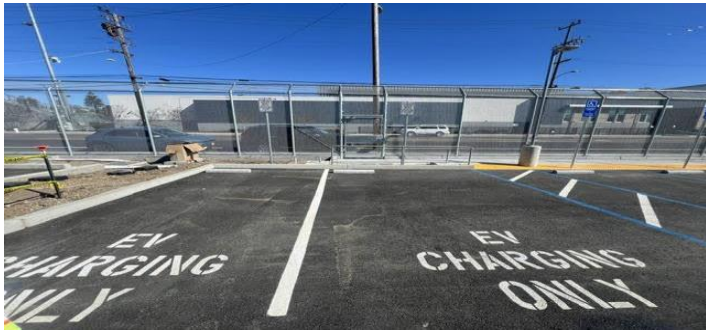

Project Profile Page  
 Scan to view project details and reports





# Districtwide Focused Investments



# Proposed Measure Y Spending Plan Priorities and Shifts



## Alignment with Facilities Master Plan & District Priorities

- **+\$4M Heat Mitigation Strategies** to expand districtwide thermal comfort, ventilation, and climate resilience efforts identified through the Facilities Master Plan → **Measure Y Program Contingency**
- **+\$1.5M Portable Removal & Site Stabilization** for safety, liability, deferred maintenance, and operational impacts at aging and vacant sites → **Measure Y Program Contingency**
- **+\$2.5M Elementary Turf Fields** to improve outdoor play, athletics, recreation, and student wellness opportunities across elementary campuses → **Measure Y Program Earned Interest**
- **+\$12M Solar & Energy Infrastructure (Board Approved)** to support the District Sustainability Policy, long-term energy resilience, and reductions to General Fund utility costs → **Measure Y Program Earned Interest**
- **+\$2M TK Expansion** to supports early childhood access, enrollment growth, and implementation of the District's TK/Early Learning strategy → **Fund 25-Developer Fees**
- **Maintain Safety Investment across the bond program** in campus security, lighting, fencing, fire/life safety, and student well-being

Demonstrates continued commitment to being strong stewards of public dollars through strategic leveraging of partnerships, grants, sustainability investments, and operational savings opportunities



## Expanding Healthy, Safe, and Climate-Responsive Schools

- Proposed **+\$4M investment** to expand districtwide heat mitigation, thermal comfort, ventilation, and climate resilience strategies identified through the 2026 Facilities Master Plan
- Aligned with [Resolution No. 2526-0226](#) — Protecting Student Health and Educational Equity Through Urgent District Wide Heat Mitigation
- Addresses growing challenges related to:
  - Extreme heat events and urban heat island impacts
  - Aging infrastructure and limited cooling capacity
  - Student wellness, indoor air quality, and classroom comfort
  - Long-term climate resilience and operational reliability
- Investments support a districtwide strategy that includes:
  - HVAC and ventilation improvements
  - Solar shade structures and outdoor greening
  - Classroom heat and air quality monitoring
  - Passive cooling and sustainable campus design strategies



# Solar & Energy Resilience Investments

Proposed **+\$12M investment in districtwide solar infrastructure** aligned with the 2026 Facilities Master Plan, Sustainability Policy, and Climate Emergency Resolution

Solar investments support:

- Reduce outdoor heat island impacts and support OUSD’s and climate policies
- Long-term General Fund savings through reduced energy costs
- Reduced strain on aging electrical infrastructure
- Future cooling and HVAC modernization supports
- Access final round of Federal incentives that will provide approximately \$3M to the “Green Revolving Fund.”

Proposed solar and battery storage strategy includes new installations, shade structures, and recommissioning existing systems while leveraging federal ITC Direct Pay opportunities and generating an estimated **\$22M in lifecycle utility savings**

Operational savings can be reinvested into student learning environments, sustainability initiatives, and long-term facilities improvements



# Transitional Kindergarten Expansion and Hub Creation

## Investing in Early Learning & Future Enrollment Growth

- **+\$2M investment** to support TK expansion aligned with the 2026 Facilities Master Plan and District early learning priorities.
- Expands access to high-quality TK spaces and supports growing enrollment demand across the district and supports the establishment of TK hubs to support families access OUSD early learning opportunities.
- Investments include:
  - Modern early learning classrooms
  - Outdoor play and learning spaces
  - Classroom Restrooms for our youngest scholars
  - Additional play structure installation that is appropriate for 4 year old age scholars.
  - Family-centered support environments
  - Infrastructure upgrades for expanded TK/PK programming
- Supports long-term enrollment growth, educational equity, and future grant and partnership opportunities





# Section Four

## Next Steps



## Next Steps

---

- Present revised Measure Y Spending Plan to the Measures B, J, and Y Independent Citizens' School Facilities Bond Oversight Committee for recommendation - **June 8, 2026**
  
- Bring Spending Plan as a Second Read and Final Recommendation to the Oakland Unified School District Facilities Committee - **June 18, 2026**
  
- Bring to Spending Plan to the Oakland Unified School District Board of Education for final approval and ratification- **June 24, 2026**



# THANK YOU

Preston Thomas, Chief Systems and Services Officer/Deputy Chief of Facilities

Sele Nadel-Hayes, Executive Director, Facilities Planning & Management

Pranita Ranbhise, Executive Director, Facilities Planning & Management

Michael Ezeh, Director, Accounting Director



**OAKLAND UNIFIED  
SCHOOL DISTRICT**

*Community Schools, Thriving Students*



# Appendix



# OUSD Facilities Funding & Masterplan History

**June 2006, Oakland voters passed Measure B, a \$435 million School Facilities Improvement Bond** which provided funding to the Oakland Unified School District (OUSD). Except for some remaining fire alarm projects, all Measure B funds have largely been spent prior to fiscal year 2019-2020.

**May 2012 Needs Assessment:** The OUSD Masterplan identified \$1.5 billion in total facility needs (File #12-1043).

**June 2012, Oakland voters passed Measure J, a \$475 million School Facilities Improvement Bond, for OUSD to enhance the educational environment for the students and communities of Oakland and better prepare students for college and jobs.** Bond funds have been allocated to upgrade science labs, classrooms, computers, and technology; improve student safety and security; repair bathrooms, electrical systems, plumbing and sewer lines; improve energy efficiency; and make seismic upgrades. Majority of Measure J Funds have been spent.

**May 2020, Needs Assessment:** The updated Masterplan revealed that district facility needs had grown to \$3.4 billion (File #19-2517).


**November 2020, Oakland voters passed Measure Y, a \$735 million School Facilities Improvement Bond,** for OUSD to provide, among other things, classroom repair and school safety improvements, upgrading classrooms, science labs and technology; improving student safety and security; repairing bathrooms, electrical systems, plumbing and sewers; and improving energy-efficiency and earthquake safety.

**May 2023, Market Escalation:** OUSD reported a 28% increase in bond project costs due to shifting market conditions. Total district needs outlined in the Masterplan subsequently rose to approximately \$4.4 billion.

**March 2025, Plan Adjustment:** The Board of Education approved Revision #3 (File #23-2330) to the Measure Y Spending Plan. This revision realigned the budget to account for market escalation, scope changes, and the long-term health of the bond.

**April 2026, Funding Draw:** OUSD successfully sold Draw 3 of the bond, raising an additional \$185 million to sustain forward momentum on all projects in the current Spending Plan.

# Background

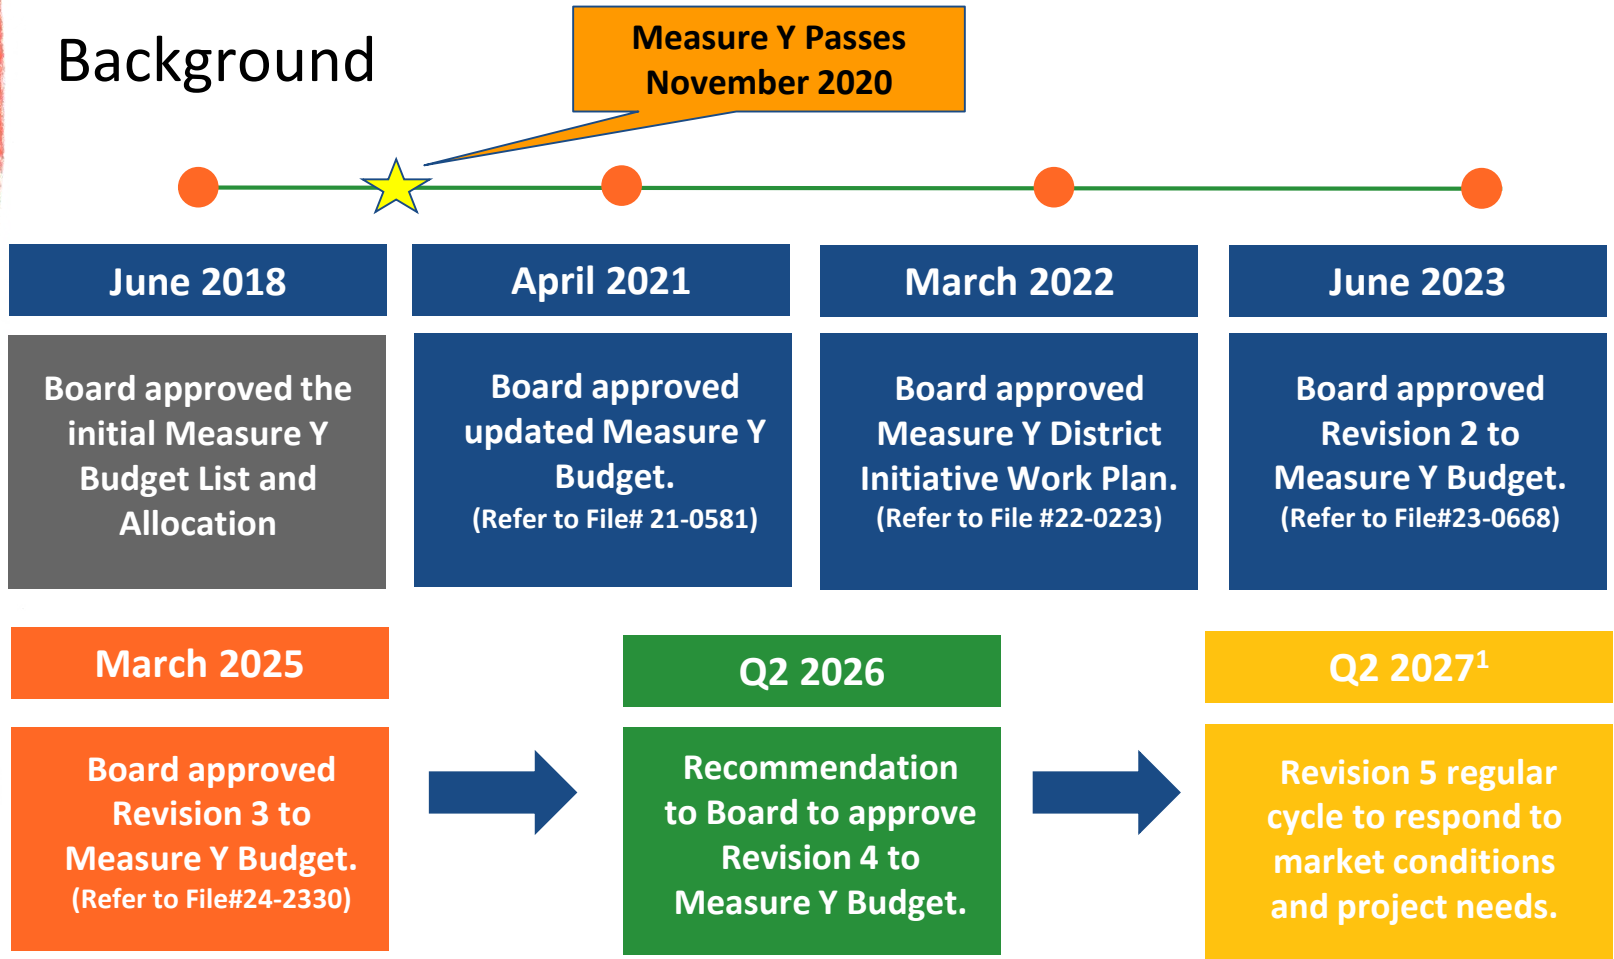

<sup>1</sup> Estimated timeline and subject to change based on changing market conditions and Board priorities.



# Expanding Our Funding Portfolio to Support Healthy, Safe, and Joyful Schools

By building a diverse portfolio of funds, the Facilities Department can thoughtfully plan, design, and build learning environments that directly support and enhance student outcomes.

